



Overview of Health Information Technology Plan





Health IT Goals

- 2 of the 7 SHIP goals are Health IT focused
 - Goal 2 Improve care coordination through the use of electronic health records (EHRs) and health data connections among PCMHs and across the medical neighborhood.
 - Goal 5 Build a statewide data analytics system that tracks progress on selected quality measures at the individual patient level, regional level, and statewide.



Our Health IT Contractors

• Idaho Health Data Exchange (IHDE) — IHDE is our health information exchange partner.

 HealthTech Solutions – HealthTech is our data analytics partner. They are establishing a connection with IHDE and are responsible for developing and providing clinical quality measure reporting.



SHIP Health IT Goals

End of Grant Year Targets

| Clinical Quality Measures | Clinics Reporting for Year 1 (By Jan 31, 2017) | Clinics Reporting for Year 2 (By Jan 31, 2018) | Clinics Reporting for Year 3 (By Jan 31, 2019) |
|------------------------------|--|--|--|
| Measures 1-4 | 55 Clinics | 110 Clinics | 165 Clinics |
| Measures 5-10 | N/A | 55 Clinics* | 110 Clinics** |
| Measures 11-16 | N/A | N/A | 55 Clinics*** |

This clarification of goals / targets needs to be approved by CMMI

^{*} Optional for Cohort 2 clinics but required for Cohort 1 clinics

^{**} Optional for Cohort 3 clinics but required for Cohort 1 & 2 clinics

^{***} Optional for Cohort 2 and 3 clinics but required for Cohort 1 clinics


| Anticipated Health IT Timelines | | | | | | | | | | |
|--|--|---------------|-----------|---|----------|----------|--------------------|---|--|--|
| (IHDE Connections and CQM Reporting timelines tied to the end of the grant year – Jan. 31st) | | | | | | | | | | |
| June | July | August | September | October | November | December | January | New Grant Yr. | | |
| | | | | | | | | | | |
| HIT Workgroup begins coordination | Workgroup Continued Efforts to Refine Year 2 Measures begins | | | | | | | | | |
| with CQM Workgroup for Year 2 Measures | Use Cases Subcommittee Meets | | | | | | | | | |
| | The second secon | vith IHDE est | ablishing | Sprint 2 with IHDE establishing connections | | | | | | |
| | | | | | | | M Reports eased | Baselines established after initial release | | |
| | | | | | | | | Page 1 | | |



Recent Activities and Next Steps



Clinic IHDE Readiness Assessment Results

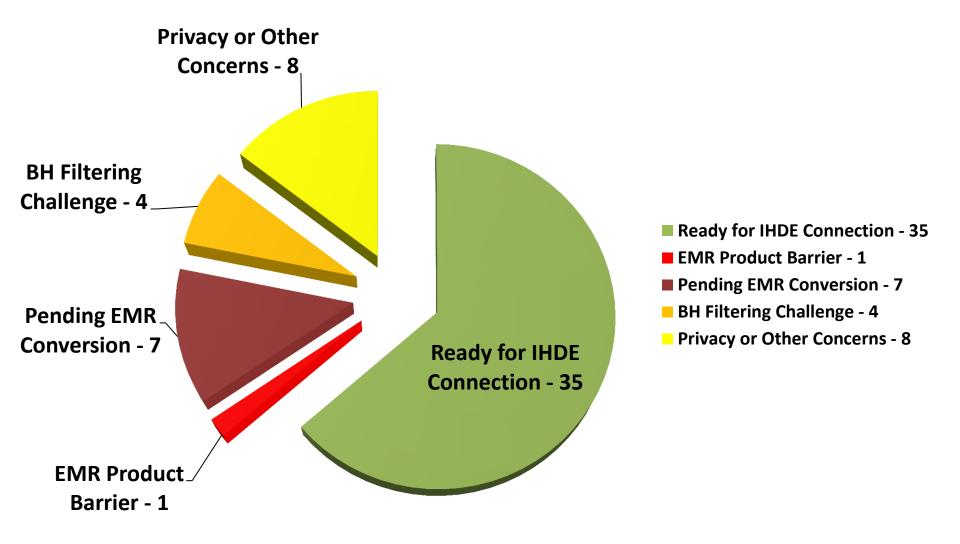



HIT Workgroup Activities

- HIT Workgroup
 - Discussed lessons learned to be applied to Cohort 2 application process
- Data Element Mapping Subcommittee
 - Redefined first 4 measures
 - Currently discussing Year 2 measures
 - Refining patient attribution methodology
- Use Cases Subcommittee
 - Met to define how specific users will use the data analytics tool from HealthTech



Idaho Health Data Exchange Recent Activities

- Conducted readiness assessment calls with all 55 clinics
- Began building clinic connections for first sprint (July – September)
- Working through connection challenges



HealthTech Solutions Recent Activities

- Hosting services have been established within a dedicated Virtual Private Cloud within Amazon Web Services
- HTS established four environments for the analytics system: Production, Training, Development, and Test
- Currently developing the measure calculation engine for first 4 measures based on sample patient CCD files and measure spec sheets



Questions

